

Agile Sprint Simulation Report


Jira Backlog, Sprint Board & Burndown Chart Analysis

Name: ADITYA MALLIKARJUN PARANDE

SRN: PES1UG24CS028


1. Jira Backlog — Epics, User Stories & Story Points

Screenshot showing the Epic panel (Shipment Posting & Bidding, Carrier Selection & Milestone Tracking, Delivery Confirmation & Escrow Payment), the Sprint 2 user stories (FM-9 to FM-12), and the Story Point badges (3, 8) visible on each story card.

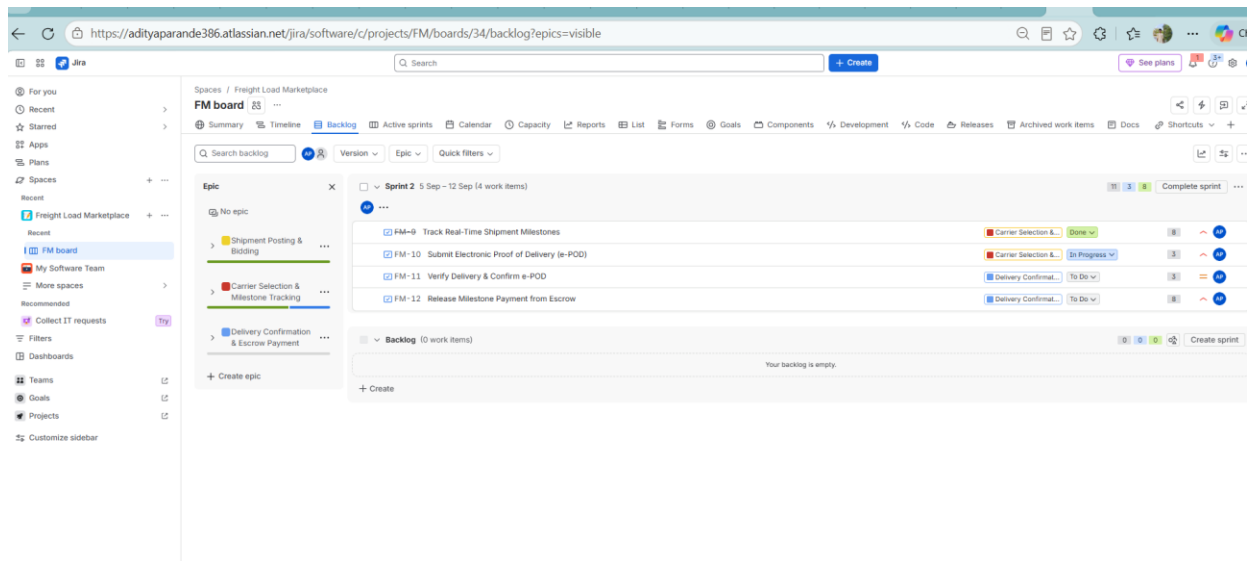


2. Sprint Board — Active Sprint View

Screenshot showing the Scrum board with three columns — To Do (FM-11: 3 pts, FM-12: 8 pts), In Progress (FM-10: 3 pts), and Done (FM-9: 8 pts) — along with the Sprint 2 header and story point badges.

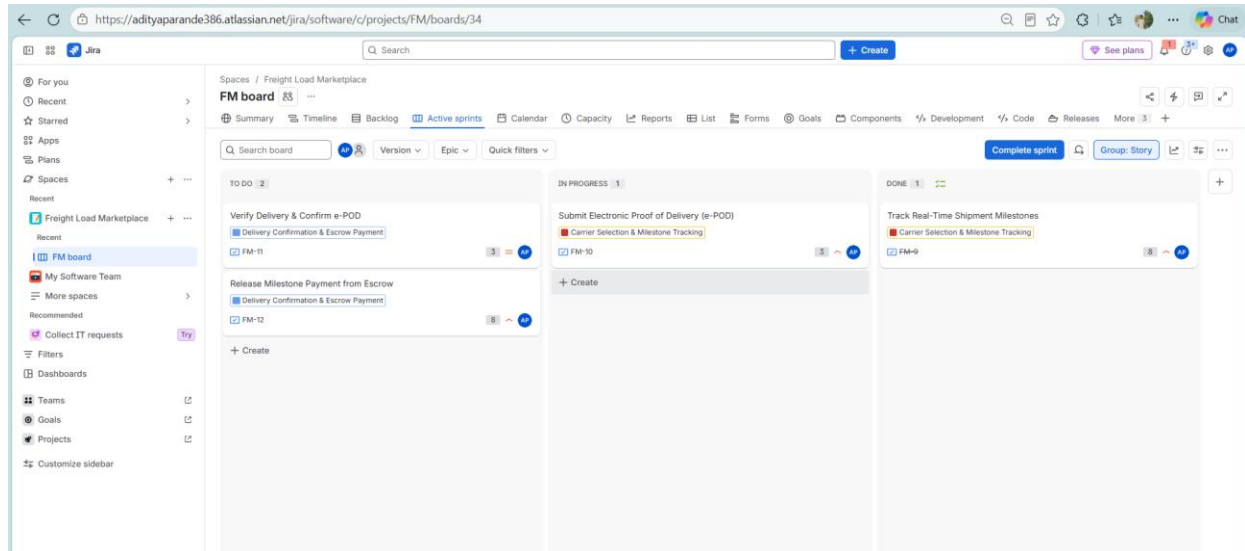

3. Burndown Chart — Sprint 2

Screenshot showing the Sprint 2 burndown chart, including the Guideline (grey line, 22 → 0), the Remaining Values (red line stepping down), the shaded weekend non-working days, and the Event Table below the graph showing the sprint start (22 pts) and completed story decrements.

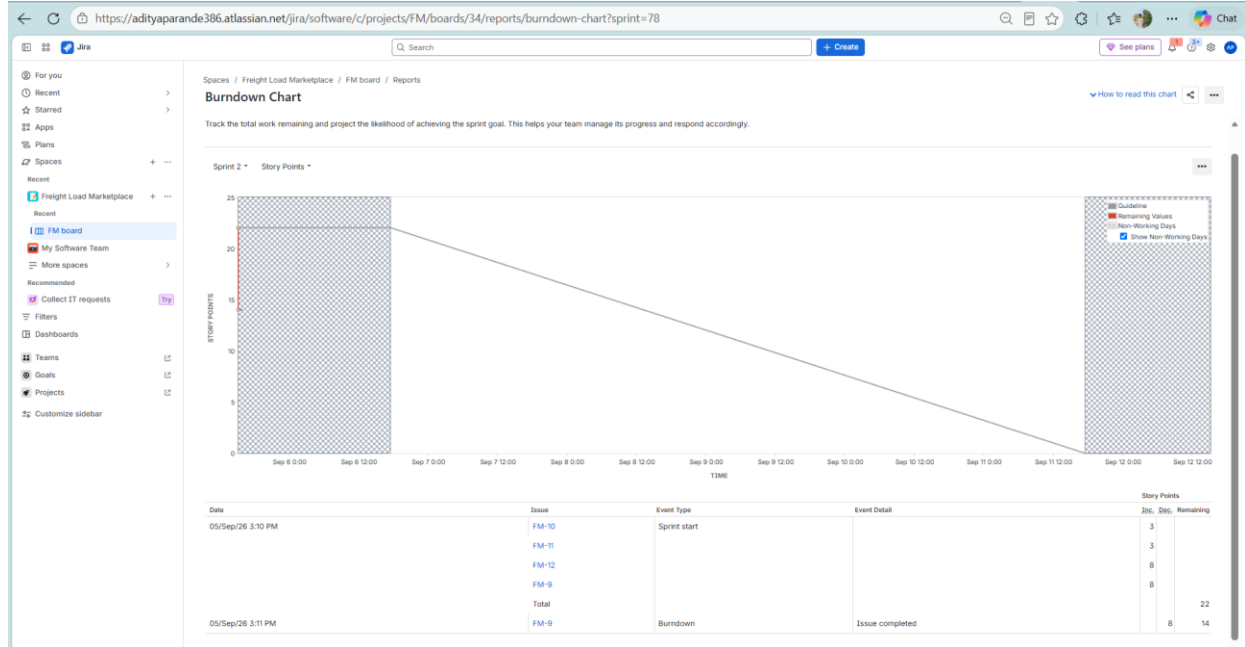

4. Reflection Questions

1. Did your estimations reflect the actual effort?

Yes. The team utilized the modified Fibonacci sequence (2, 3, 5, 8) to size user stories based on complexity, effort, and risk rather than simple hours:

- **Low Complexity (2 Story Points):** Read-only and filtering items like View Available Freight Loads (FM-5) and View Bid Status (FM-7) involved standard database querying and UI display with minimal uncertainty.
- **Medium Complexity (5 Story Points):** Core transactional stories like Post Freight Load (FM-2), Submit Carrier Bid (FM-6), and Select Winning Bid (FM-8) required multi-field validation, bidding logic, and real-time state transitions.
- **High Complexity (8 Story Points):** Stories such as Track Real-Time Milestones (FM-9) and Release Milestone Payment from Escrow (FM-12) had high uncertainty due to external IoT/GPS telemetry integration and strict financial banking compliance rules.

2. Was your backlog well-prioritized?

Yes, the backlog followed the Value vs. Dependency model aligned with the freight lifecycle:

- **Phase 1 — Pre-requisites (Sprint 1):** In an inter-city freight marketplace, loads must be posted (FM-2), searched (FM-5), and bid on (FM-6) before any shipment contract can be finalized (FM-8). Scheduling these in Sprint 1 established the foundation.
- **Phase 2 — Execution & Settlement (Sprint 2):** In-transit GPS tracking (FM-9), digital proof of delivery upload (FM-10), consignee verification (FM-11), and escrow payment payout (FM-12) were scheduled sequentially after the matching contract is created. This dependency-based sequencing eliminated workflow bottlenecks and ensured each sprint produced a functional increment.

3. How did your simulated sprint align with your plan?

Sprint 1 was planned for 19 Story Points across 5 user stories for a 1-week timebox.

- All 5 stories were committed at sprint start, establishing an initial baseline of 19 Story Points against the burndown guideline.
- Tasks progressed across To Do → In Progress → Done, burning down the scope to zero.
- Because this was simulated in a laboratory session rather than across 7 calendar days, the burndown line displays rapid step-downs on the simulation date rather than a gradual daily slope. In a real agile environment, this pattern represents late-sprint batch verification, highlighting the importance of daily stand-ups and continuous integration.

4. What insights did the burndown chart give about your team's capacity?

- **Baseline Velocity:** Completing 19 Story Points in Sprint 1 established an empirical velocity baseline for the team.
- **Capacity Forecasting for Sprint 2:** Sprint 2 was estimated at 22 Story Points. Comparing this against the 19-point baseline immediately flags a slight overallocation (+15%), warning the team to either split high-complexity tasks (FM-12, 8 pts) or anticipate scope carry-over.
- **Scope Control Visibility:** The chart clearly distinguishes between the initial committed scope (Sprint start) and the actual completion trend, giving visibility into scope control and team throughput across the sprint.
